

High School Addition & Remodeling

Activity Report

January 8, 2018

OBJECTIVE:

RENOVATION OF EXISTING HIGH SCHOOL WITH FIELDHOUSE & SECURE ENTRY ADDITION

SCOPE:

DESIGN AND CONSTRUCT FOR FINAL OCCUPANCY FALL 2018

KEITH HILTS
DISTRICT ADMINISTRATOR
715-682-7080
KHILTS@SDAK.12.NET

RECENT ACTIVITY:




- 75% shop drawings submitted
- 74% shop drawings reviewed
- Continued sheetrock in office and commons
- Continued soffit framing
- Worked on fire alarm in fieldhouse
- Worked on gym equipment connections
- Worked on egress lighting in fieldhouse
- Continued piping rough in for commons and office
- Continued work in mezzanine
- Continued installing gym equipment
- Continued painting in fieldhouse
- Finished EIFS on west side

CRITICAL UPCOMING EVENTS:

- Complete team room rough ins
- Air balancing in fieldhouse
- Start ceiling grid and tile in commons
- Work on sprinkler rough in for commons

KEY DATES:

- Next meeting: 1-10-18

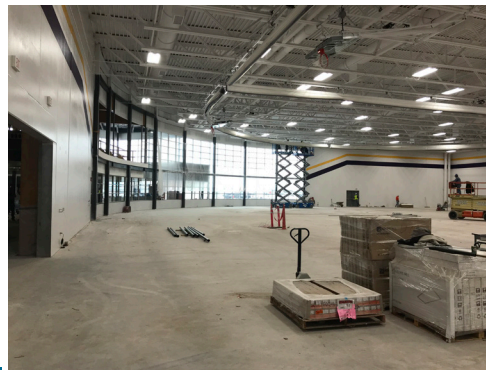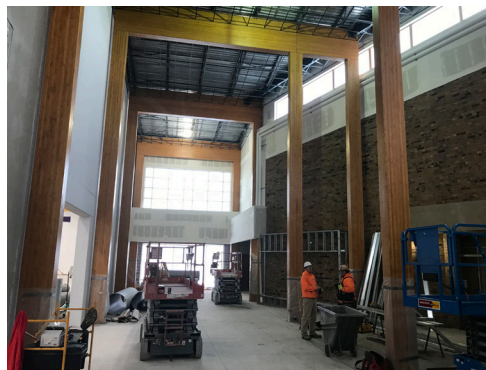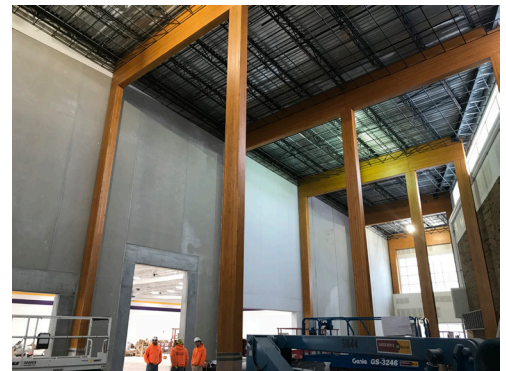

Construction: Phase I
Construction: Phase IA
Construction: Phase II

Occupancy

Occupancy

Occupancy

Construction: Phase III

Occupancy

April 2017	May 2017	June 2017	July 2017	Aug 2017	Sept 2017	Oct 2017	Nov 2017	Dec 2017	Jan 2018	Feb 2018	March 2018	April 2018	May 2018	June 2018	July 2018	Aug 2018	Sept 2018



We are here
