

High School Addition & Remodeling

Activity Report

February 5, 2018

OBJECTIVE:

RENOVATION OF EXISTING HIGH SCHOOL WITH FIELDHOUSE & SECURE ENTRY ADDITION

SCOPE:

DESIGN AND CONSTRUCT FOR FINAL OCCUPANCY FALL 2018

KEITH HILTS
DISTRICT ADMINISTRATOR
715-682-7080
KHILTS@SDAK.12.NET

RECENT ACTIVITY:



- 80% shop drawings submitted
- 70% shop drawings reviewed
- Framed ceiling for concession
- Started sheetrock at concession
- Started glu-lams at east entry
- Worked on lights in mezzanine mechanical room
- Finished concession electrical rough-in
- Worked on concession rough-in
- Tested plumbing in concession
- Finished taping in commons
- Continued taping in office
- Finished dry wall on mezzanine
- Continued painting walls and soffits in commons
- Started terrazzo on west of commons
- Continued EIFS on high elevation of commons
- Set remainder of storefront at office
- Finished bathrooms by elevator

CRITICAL UPCOMING EVENTS:

- Work on plumbing fixtures in team rooms
- Continue ductwork in mezzanine
- Hang lights in commons
- Finish painting in commons and by elevator
- Continue athletic floor

KEY DATES:

- Next meeting: 2-7-18

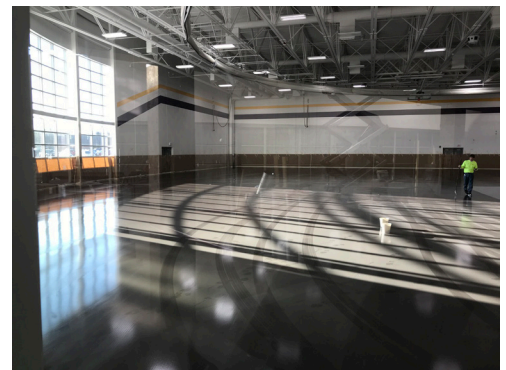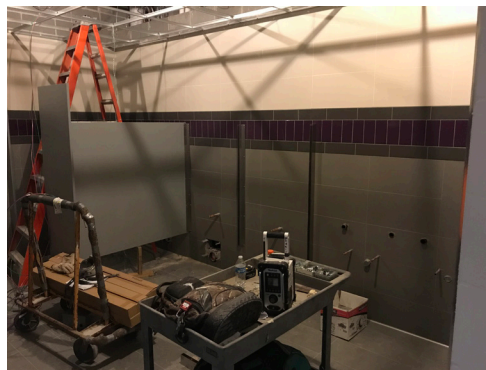

Construction: Phase I
Construction: Phase IA
Construction: Phase II

Occupancy

Occupancy

Occupancy

Construction: Phase III

Occupancy

April 2017 May 2017 June 2017 July 2017 Aug 2017 Sept 2017 Oct 2017 Nov 2017 Dec 2017 Jan 2018 Feb 2018 March 2018 April 2018 May 2018 June 2018 July 2018 Aug 2018 Sept 2018

↑
We are here
