

OBJECTIVE:

RENOVATION OF EXISTING HIGH SCHOOL WITH FIELDHOUSE & SECURE ENTRY ADDITION

SCOPE:

DESIGN AND CONSTRUCT FOR FINAL OCCUPANCY FALL 2018

KEITH HILTS
DISTRICT ADMINISTRATOR
715-682-7080
KHILTS@SDAK.12.NET

RECENT ACTIVITY:



- 88% shop drawings submitted
- 88% shop drawings reviewed
- Finished glu-lams at east entrance
- Finished sheetrock on concession walls
- Installed lights and controls in areas A1 and A2
- Worked on cabinet heating in team rooms
- Insulated fieldhouse mechanical room
- Continued painting walls and soffits in office
- Continued terrazzo in commons
- Installed EIFS on low elevation on east side
- Continued sprinkler work in office
- Continued control rough-in and wire in mechanical room
- Installed overhead doors at fieldhouse storage rooms
- Roofing at entry canopies
- Continued installing ceiling grid in office
- Started polishing in west commons
- Finish courts in fieldhouse
- Start work on track

CRITICAL UPCOMING EVENTS:

- Elevator inspection set for March 12th
- Punch list set for March 14th
- Inspection set for March 19th

KEY DATES:

- Next meeting: 2-21-18

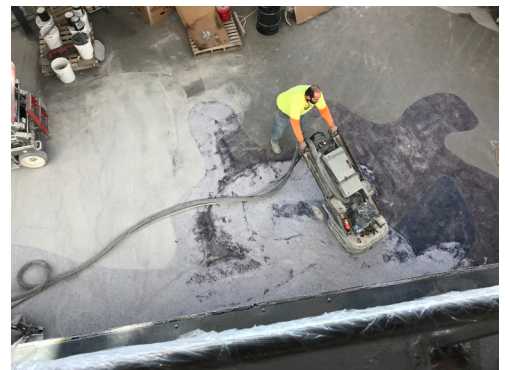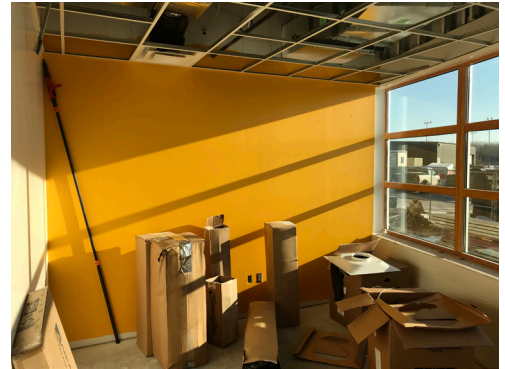

Construction: Phase I
Construction: Phase IA
Construction: Phase II

Occupancy

Occupancy

Occupancy

Construction: Phase III

Occupancy

April 2017	May 2017	June 2017	July 2017	Aug 2017	Sept 2017	Oct 2017	Nov 2017	Dec 2017	Jan 2018	Feb 2018	March 2018	April 2018	May 2018	June 2018	July 2018	Aug 2018	Sept 2018

↑
We are here
