

OBJECTIVE:

RENOVATION OF EXISTING HIGH SCHOOL WITH FIELDHOUSE & SECURE ENTRY ADDITION

SCOPE:

DESIGN AND CONSTRUCT FOR FINAL OCCUPANCY FALL 2018

KEITH HILTS
DISTRICT ADMINISTRATOR
715-682-7080
KHILTS@SDAK.12.NET

RECENT ACTIVITY:


- 92% shop drawings submitted
- 92% shop drawings reviewed
- Finished column covers
- Cleaned and demobilized
- Installed display cases
- Worked on fire alarms
- Installed grilles and diffusers
- Installed plumbing fixtures
- Installed base in commons
- Installed solid surface tops and sills
- Cleaned air handler units
- Installed coiling doors at shipping and fieldhouse mechanical rooms
- Finished installed mezzanine hand rails

CRITICAL UPCOMING EVENTS:

- Install aluminum doors and hardware at fieldhouse entrance
- Finish sprinkler system in mechanical rooms
- Elevator inspection set for March 19th
- Punch list set for March 21th
- Inspection set for March 19th
- All as-builts should be completed no later than March 23rd

KEY DATES:

- Next meeting: 3-21-18

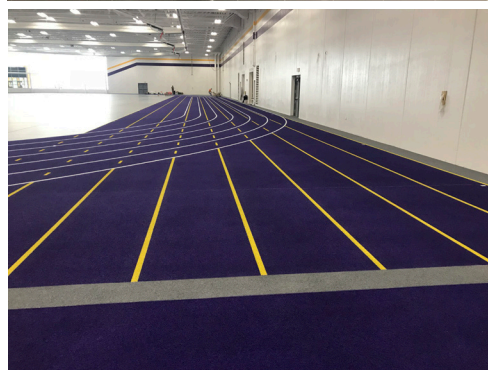

Construction: Phase I
Construction: Phase IA
Construction: Phase II

Occupancy

Occupancy

Occupancy

Construction: Phase III

Occupancy

April 2017	May 2017	June 2017	July 2017	Aug 2017	Sept 2017	Oct 2017	Nov 2017	Dec 2017	Jan 2018	Feb 2018	March 2018	April 2018	May 2018	June 2018	July 2018	Aug 2018	Sept 2018

↑
We are here
