

High School Addition & Remodeling

Activity Report

July 17, 2017

OBJECTIVE:

RENOVATION OF EXISTING HIGH SCHOOL WITH FIELDHOUSE & SECURE ENTRY ADDITION

SCOPE:

DESIGN AND CONSTRUCT FOR FINAL OCCUPANCY FALL 2018

KEITH HILTS
DISTRICT ADMINISTRATOR
715-682-7080
KHILTS@SDAK.12.NET

RECENT ACTIVITY:


- 40% shop drawings submitted
- 39% shop drawings reviewed
- Removed IMC roof and installed steel framing.
- Continued sheetrock and started painting Area C1 & C2.
- Excavation for last foundations.
- Installed electrical panels and started pulling wire.
- Installed VAV boxes, wiring and started installing diffusers.
- Started installing ceilings.
- Started insalling ceramic tile.
- Completed CMU walls in team rooms.

CRITICAL UPCOMING EVENTS:

- Finish framing IMC high walls.
- Set precast planck at Fieldhouse.
- Install IMC roofing.
- Install split-joint in existing gym.

KEY DATES:

- Next meeting 7-19-17

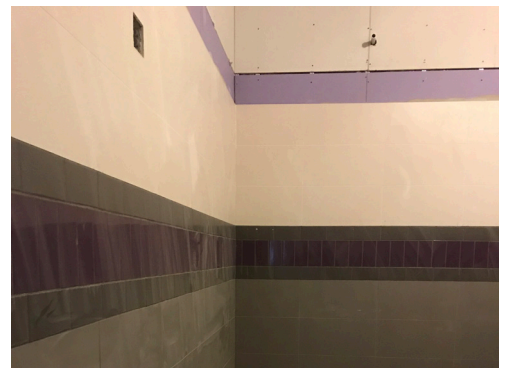

Construction: Phase I
Construction: Phase IA
Construction: Phase II

Occupancy

Occupancy

Occupancy

Construction: Phase III

Occupancy

April 2017	May 2017	June 2017	July 2017	Aug 2017	Sept 2017	Oct 2017	Nov 2017	Dec 2017	Jan 2018	Feb 2018	March 2018	April 2018	May 2018	June 2018	July 2018	Aug 2018	Sept 2018



We are here
