

High School Addition & Remodeling

Activity Report

August 14, 2017

OBJECTIVE:

RENOVATION OF EXISTING HIGH SCHOOL WITH FIELDHOUSE & SECURE ENTRY ADDITION

SCOPE:

DESIGN AND CONSTRUCT FOR FINAL OCCUPANCY FALL 2018

KEITH HILTS
DISTRICT ADMINISTRATOR
715-682-7080
KHILTS@SDAK.12.NET

RECENT ACTIVITY:


- 49% shop drawings submitted
- 49% shop drawings reviewed
- Installed marker boards, doors and hardware in classrooms.
- Fine grading and black dirt installed at north parking lot.
- Installed precast plank mezzanine.
- Installed steel bar joists at Fieldhouse.
- Installed linear metal ceiling and lighting in Flex spaces.
- Completed tile installation in east and west corridors.
- Painting in classrooms.

CRITICAL UPCOMING EVENTS:

- Pour concrete topping on mezzanine.
- Finish electrical devices and fire alarm.
- Pave parking lot.
- Paint roof deck and joists.

KEY DATES:

- Next meeting: 8-16-17
- Punch List: 8-16-17
- Testing and Balancing: 8-18-17

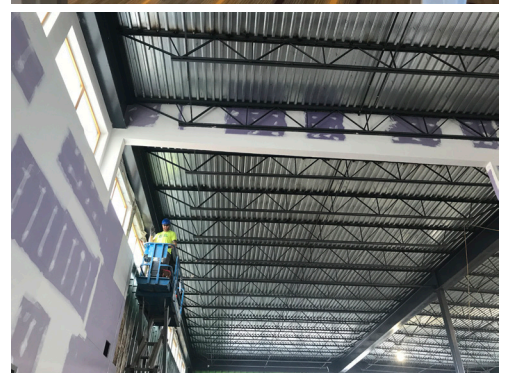

Construction: Phase I
Construction: Phase IA
Construction: Phase II

Occupancy

Occupancy

Occupancy

Construction: Phase III

Occupancy

April 2017	May 2017	June 2017	July 2017	Aug 2017	Sept 2017	Oct 2017	Nov 2017	Dec 2017	Jan 2018	Feb 2018	March 2018	April 2018	May 2018	June 2018	July 2018	Aug 2018	Sept 2018



We are here
