

Marengo Valley Elementary Remodeling & Addition

Activity Report

August 28, 2017

OBJECTIVE:

RENOVATION AND ADDITION TO
MARENGO VALLEY ELEMENTARY
SCHOOL

SCOPE:

DESIGN AND CONSTRUCT FOR FALL
2017 OCCUPANCY

KEITH HITLS
DISTRICT ADMINISTRATOR
715-682-7080
KHILTS@SDAK.12.NET

RECENT ACTIVITY:


- 83% shop drawings submitted
- 82% shop drawings reviewed
- Prepped for sod.
- Installed casework.
- Final cleaning.
- Installed ceiling grid in Art Room.
- Installed ductwork in Multi-purpose room.
- Worked on Fire Alarm.
- Installed finishes throughout.

CRITICAL UPCOMING EVENTS:

- Install insulation and siding on Multi-purpose room.
- Install window sills and cut in sinks.

KEY DATES:

- Next meeting - 8-31-17

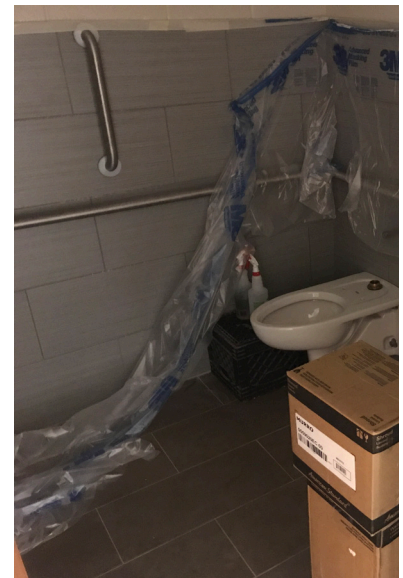

Construction: Phase I

Occupancy

Construction: Phase IA

Occupancy

Construction: Phase 2

Occupancy

4/2017

5/2017

6/2017

7/2017

8/2017

9/2017

10/2017

11/2017


We are here
