

High School Addition & Remodeling

Activity Report

October 9, 2017

OBJECTIVE:

RENOVATION OF EXISTING HIGH SCHOOL WITH FIELDHOUSE & SECURE ENTRY ADDITION

SCOPE:

DESIGN AND CONSTRUCT FOR FINAL OCCUPANCY FALL 2018

KEITH HILTS
DISTRICT ADMINISTRATOR
715-682-7080
KHILTS@SDAK.12.NET

RECENT ACTIVITY:


- 58% shop drawings submitted
- 56% shop drawings reviewed
- Poured Fieldhouse floor
- Stud framed and rocked at curtain wall
- Detailed glulams
- Washed precast
- Installed receptacles and lights in IMC
- Set joist in commons
- Laid up east wall on mezzanine
- Continued painting IMC
- Fieldhouse mechanical room

CRITICAL UPCOMING EVENTS:

- Install reception desk and display cases
- Grade commons area
- Fieldhouse ducts and roof drains
- Receptacles and lights in IMC
- Commons roof

KEY DATES:

- School began: 9-11-17
- Next meeting: 10-11-17

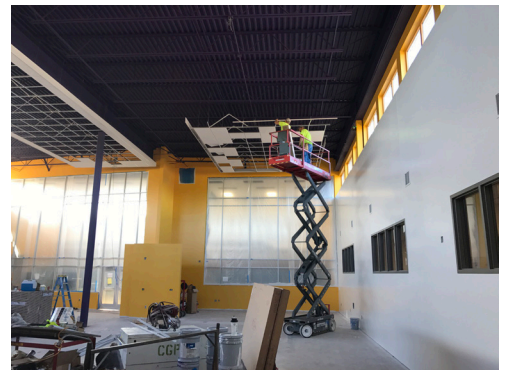

Construction: Phase I
Construction: Phase IA
Construction: Phase II

Occupancy

Occupancy

Occupancy

Construction: Phase III

Occupancy

April 2017	May 2017	June 2017	July 2017	Aug 2017	Sept 2017	Oct 2017	Nov 2017	Dec 2017	Jan 2018	Feb 2018	March 2018	April 2018	May 2018	June 2018	July 2018	Aug 2018	Sept 2018



We are here
