

High School Addition & Remodeling

Activity Report

November 6, 2017

OBJECTIVE:

RENOVATION OF EXISTING HIGH SCHOOL WITH FIELDHOUSE & SECURE ENTRY ADDITION

SCOPE:

DESIGN AND CONSTRUCT FOR FINAL OCCUPANCY FALL 2018

KEITH HILTS
DISTRICT ADMINISTRATOR
715-682-7080
KHILTS@SDAK.12.NET

RECENT ACTIVITY:


- 65% shop drawings submitted
- 64% shop drawings reviewed
- Continued curtain walls and wood windows
- Poured slab for commons and office
- Continued exterior stud walls
- Continue spiral duct in fieldhouse
- Finished brick at fieldhouse and offices
- Furniture Delivered to IMC

CRITICAL UPCOMING EVENTS:

- Continue fire suppression rough-in for fieldhouse
- Program temperature controls in mechanical room
- Spray foam parapet walls

KEY DATES:

- School began: 9-11-17
- Next meeting: 11-08-17
- IMC Complete: 11-01-17

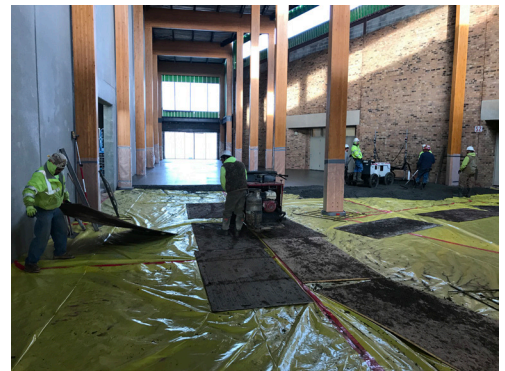

Construction: Phase I
Construction: Phase IA
Construction: Phase II

Occupancy

Occupancy

Occupancy

Construction: Phase III

Occupancy

April 2017	May 2017	June 2017	July 2017	Aug 2017	Sept 2017	Oct 2017	Nov 2017	Dec 2017	Jan 2018	Feb 2018	March 2018	April 2018	May 2018	June 2018	July 2018	Aug 2018	Sept 2018
------------	----------	-----------	-----------	----------	-----------	----------	----------	----------	----------	----------	------------	------------	----------	-----------	-----------	----------	-----------



We are here
