

# High School Addition & Remodeling

Activity Report

December 18, 2017

## OBJECTIVE:

RENOVATION OF EXISTING HIGH SCHOOL WITH FIELDHOUSE & SECURE ENTRY ADDITION

## SCOPE:

DESIGN AND CONSTRUCT FOR FINAL OCCUPANCY FALL 2018

KEITH HILTS  
DISTRICT ADMINISTRATOR  
715-682-7080  
KHILTS@SDAK.12.NET

## RECENT ACTIVITY:


- 72% shop drawings submitted
- 71% shop drawings reviewed
- Started framing interior partitions in office
- Finished wood panels in IMC
- Finished temporary enclosures
- Finished piping roof drains
- Continued glazing field house curtain wall & H windows
- Installed door hardware in IMC
- Started sheetrock in office
- Demo doors in existing gym
- Hung lights in fieldhouse
- Fans and gym equipment in fieldhouse
- Continued installing wood window at office
- Started up boiler 2 and rest of AHU

## CRITICAL UPCOMING EVENTS:

- Access Security rectify security system
- Check fieldhouse floor tolerances

## KEY DATES:

- Next meeting: 1-3-17

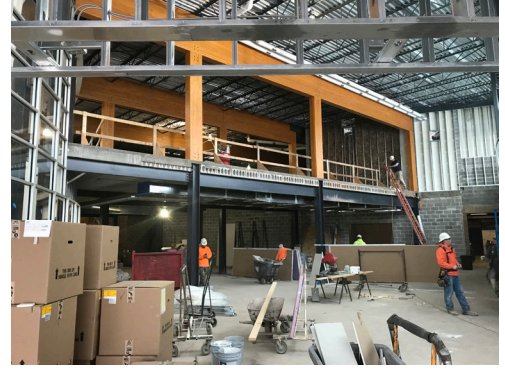

Construction: Phase I  
Construction: Phase IA  
Construction: Phase II

Occupancy

Occupancy

Occupancy

Construction: Phase III

Occupancy

April 2017 May 2017 June 2017 July 2017 Aug 2017 Sept 2017 Oct 2017 Nov 2017 Dec 2017 Jan 2018 Feb 2018 March 2018 April 2018 May 2018 June 2018 July 2018 Aug 2018 Sept 2018

We are here
