

Middle School Addition & Remodeling

Activity Report

August 6, 2018

OBJECTIVE:

RENOVATION OF EXISTING MIDDLE SCHOOL WITH IMC, COMMONS AND CLASSROOM ADDITIONS

SCOPE:

DESIGN AND CONSTRUCT FOR FINAL OCCUPANCY FALL 2018

KEITH HILTS
DISTRICT ADMINISTRATOR
715-682-7080
KHILTS@SDAK.12.NET

RECENT ACTIVITY:


- Continued setting casework
- Started framing and sheathing for metal wall panels
- Continued installing electrical devices and light fixtures
- Finished work in mechanical rooms
- Started flooring in IMC
- Set columns for canopy
- Finished painting in tech-ed and offices
- Started painting soffits in flex spaces and computer lab
- Started sheetrock in art room

CRITICAL UPCOMING EVENTS:

- Continue setting casework
- Start brick for canopy
- Complete work with Xcel for transformer replacement
- Continue sheetrock and tape in art room
- Continue installing flooring

KEY DATES:

- Next meeting: 8-8-18

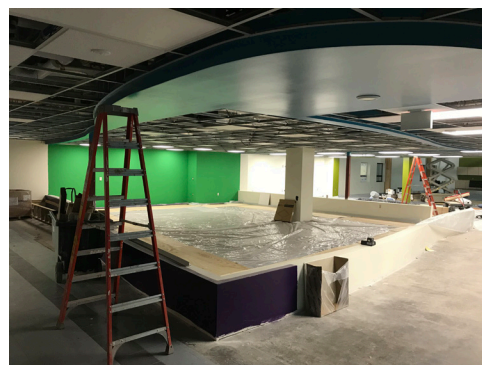

Construction: Phase 1

Construction: Phase 2

Construction: Phase 3

Occupancy

3/2017

4/2017

5/2017

6/2017

7/2017

8/2017

9/2017



We are here
