

Lake Superior Elementary Remodeling & Additions

Activity Report

August 28, 2017

OBJECTIVE:

RENOVATION AND ADDITIONS
TO LAKE SUPERIOR ELEMENTARY
SCHOOL

SCOPE:

DESIGN AND CONSTRUCT FOR FALL
2017 OCCUPANCY

KEITH HILTS
DISTRICT ADMINISTRATOR
715-682-7080
KHILTS@SDAK.12.NET

RECENT ACTIVITY:


- 78% shop drawings submitted
- 78% shop drawings reviewed
- Continued installing block walls and poured slab in Area H.
- Installed plumbing fixtures, drains and cleanouts in Area H.
- Tested fire alarm and installed power and low voltage wiring in office.
- Finished AHU 15 and startup equipment.
- Finished flooring in Areas C & E.
- Continue installing window sills, markerboards, doors and hardware.

CRITICAL UPCOMING EVENTS:

- Install sod.
- Air balancing.
- Start setting structural steel in Area H.

KEY DATES:

- Next meeting 8-30-17
- Staff Move-in: 8-28-17

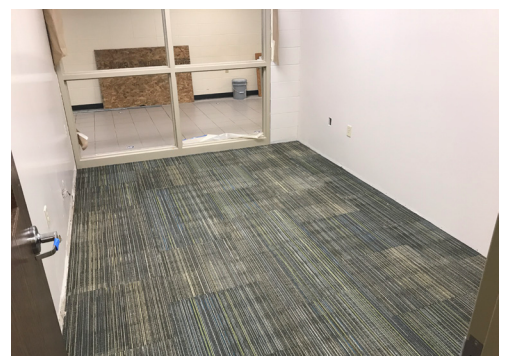

Construction: Phase I

Occupancy

Construction: Phase IA

Occupancy

Construction: Phase 2

Occupancy

4/2017

5/2017

6/2017

7/2017

8/2017

9/2017

10/2017

11/2017

↑
We are here
