

Lake Superior Elementary Remodeling & Additions

Activity Report

November 6, 2017

OBJECTIVE:

RENOVATION AND ADDITIONS
TO LAKE SUPERIOR ELEMENTARY
SCHOOL

SCOPE:

DESIGN AND CONSTRUCT FOR FALL
2017 OCCUPANCY

KEITH HILTS
DISTRICT ADMINISTRATOR
715-682-7080
KHILTS@SDAK.12.NET

RECENT ACTIVITY:


- 88% shop drawings submitted
- 88% shop drawings reviewed
- Continued painting walls, accent walls and frames
- Started plumbing fixtures in bathrooms
- Dropped diffusers and grilles in ceiling grid
- Started lights in ceilings
- Continue cabinets in classrooms and kitchen
- Installed exterior hollow metal doors

CRITICAL UPCOMING EVENTS:

- Brick delivery
- Finish roof edge metal
- Finish EIFS on mezzanine

KEY DATES:

- School began 9-11-17
- Next meeting: 11-08-17
- Punch List: 11-15-17

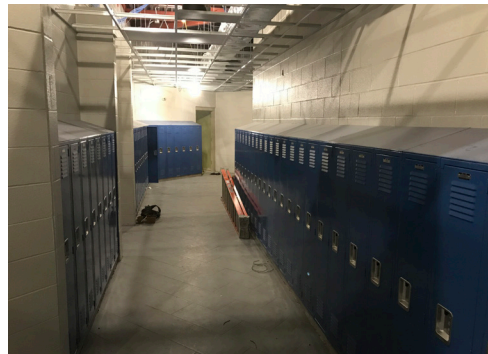

Construction: Phase I

Occupancy

Construction: Phase IA

Occupancy

Construction: Phase 2

Occupancy

4/2017

5/2017

6/2017

7/2017

8/2017

9/2017

10/2017

11/2017

↑
We are here
