

Lake Superior Elementary Remodeling & Additions

Activity Report

October 9, 2017

OBJECTIVE:

RENOVATION AND ADDITIONS
TO LAKE SUPERIOR ELEMENTARY
SCHOOL

SCOPE:

DESIGN AND CONSTRUCT FOR FALL
2017 OCCUPANCY

KEITH HILTS
DISTRICT ADMINISTRATOR
715-682-7080
KHILTS@SDAK.12.NET

RECENT ACTIVITY:


- 82% shop drawings submitted
- 82% shop drawings reviewed
- Continued laying brick in area H
- Continued duckwork rough-in in area H
- Continued overhead rough-in in area H
- Decking area H roof
- Started roofing in area H

CRITICAL UPCOMING EVENTS:

- Dry out block for painting in area H
- Finish rubbing block
- Install windows in area H
- Start EIFS in area H

KEY DATES:

- School began 9-11-17
- Next meeting: 10-11-17

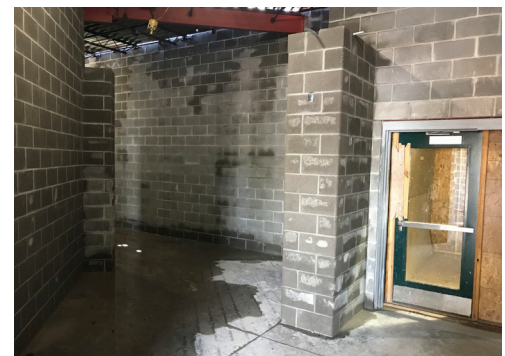

Construction: Phase I

Occupancy

Construction: Phase IA

Occupancy

Construction: Phase 2

Occupancy

4/2017

5/2017

6/2017

7/2017

8/2017

9/2017

10/2017

11/2017

↑
We are here
