

High School Addition & Remodeling

Activity Report

January 22, 2018

OBJECTIVE:

RENOVATION OF EXISTING HIGH SCHOOL WITH FIELDHOUSE & SECURE ENTRY ADDITION

SCOPE:

DESIGN AND CONSTRUCT FOR FINAL OCCUPANCY FALL 2018

KEITH HILTS
DISTRICT ADMINISTRATOR
715-682-7080
KHILTS@SDAK.12.NET

RECENT ACTIVITY:


- 78% shop drawings submitted
- 76% shop drawings reviewed
- Continued glu-lams and deck at entrances
- Framed and sheetrocked concession area walls
- Continued ductwork in west side of commons
- Continued mezzanine ductwork
- Worked on fieldhouse mechanical rooms
- Continued taping walls in office and soffits in commons
- Continued painting deck and joists above mezzanine
- Continued grid and tile on east side of commons
- Installed frames between fieldhouse and commons
- Continued EIFS on east side of commons

CRITICAL UPCOMING EVENTS:

- Start athletic floor
- Continue elevator install
- Meeting with city to discuss boulevard on Beaser Ave

KEY DATES:

- Next meeting: 1-24-18

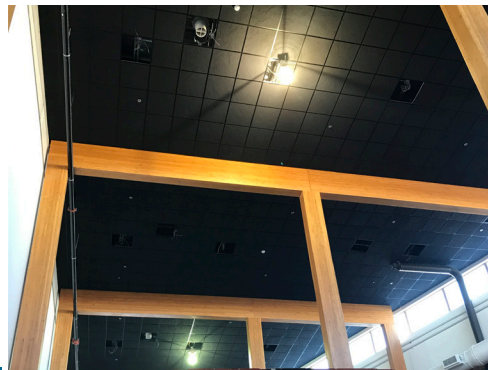

Construction: Phase I
Construction: Phase IA
Construction: Phase II

Occupancy

Occupancy

Occupancy

Construction: Phase III

Occupancy

April 2017	May 2017	June 2017	July 2017	Aug 2017	Sept 2017	Oct 2017	Nov 2017	Dec 2017	Jan 2018	Feb 2018	March 2018	April 2018	May 2018	June 2018	July 2018	Aug 2018	Sept 2018

↑
We are here
