

High School Addition & Remodeling

Activity Report

March 5, 2018

OBJECTIVE:

RENOVATION OF EXISTING HIGH SCHOOL WITH FIELDHOUSE & SECURE ENTRY ADDITION

SCOPE:

DESIGN AND CONSTRUCT FOR FINAL OCCUPANCY FALL 2018

KEITH HILTS
DISTRICT ADMINISTRATOR
715-682-7080
KHILTS@SDAK.12.NET

RECENT ACTIVITY:



- 88% shop drawings submitted
- 88% shop drawings reviewed
- Covered and protected polished terrazzo
- Finished glu-lams at east entrance
- Installed casework at office
- Worked on plumbing fixtures
- Installed railing around mezzanine
- Painted concession walls
- Dropped ceiling tile in office
- Polished terrazzo in west commons
- Continued sprinkler work under mezzanine

CRITICAL UPCOMING EVENTS:

- Work on lights and devices in areas A1 and A2
- Finish painting staircase
- Continue working on track
- Clean fieldhouse and remove material
- Air balancing will be March 12th
- Elevator inspection set for March 12th
- Punch list set for March 14th
- Inspection set for March 19th

KEY DATES:

- Next meeting: 3-7-18

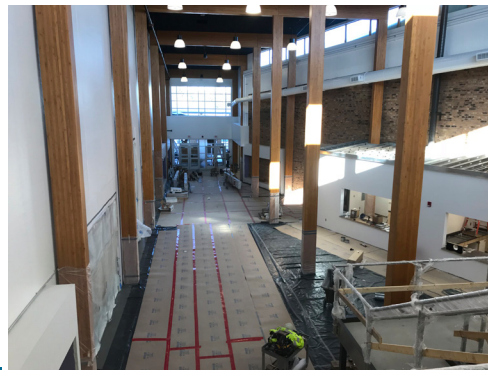

↑
We are here
