

# High School Addition & Remodeling

Activity Report

April 2, 2018

## OBJECTIVE:

RENOVATION OF EXISTING HIGH SCHOOL WITH FIELDHOUSE & SECURE ENTRY ADDITION

## SCOPE:

DESIGN AND CONSTRUCT FOR FINAL OCCUPANCY FALL 2018

KEITH HILTS  
DISTRICT ADMINISTRATOR  
715-682-7080  
KHILTS@SDAK.12.NET

## RECENT ACTIVITY:



- 92% shop drawings submitted
- 92% shop drawings reviewed
- Installed casework
- Installed map on concessions
- Installed lights in display cases
- Painted doors and walls
- Installed flooring in elevator, vestibules and concessions
- Installed wood doors and hardware
- Finished waxing terrazzo
- Final cleaning
- Completed fire suppression inspection
- Completed State DSPS inspection

## CRITICAL UPCOMING EVENTS:

- Install letters at reception desk
- Complete punch list items for Phase II
- Work in Charter Space

## KEY DATES:

- Next meeting: 3-21-18

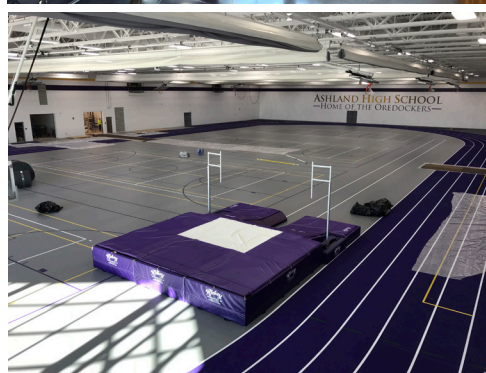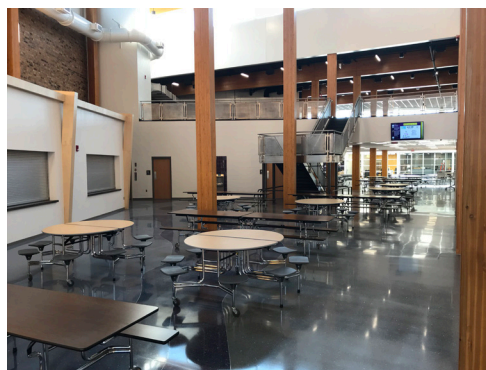

Construction: Phase I  
Construction: Phase IA  
Construction: Phase II

Occupancy

Occupancy

Occupancy

Construction: Phase III

Occupancy

April 2017	May 2017	June 2017	July 2017	Aug 2017	Sept 2017	Oct 2017	Nov 2017	Dec 2017	Jan 2018	Feb 2018	March 2018	April 2018	May 2018	June 2018	July 2018	Aug 2018	Sept 2018
------------	----------	-----------	-----------	----------	-----------	----------	----------	----------	----------	----------	------------	------------	----------	-----------	-----------	----------	-----------

↑  
We are here
