

Marengo Valley Elementary Remodeling & Addition

Activity Report

May 8, 2017

OBJECTIVE:

RENOVATION AND ADDITION TO
MARENGO VALLEY ELEMENTARY
SCHOOL

SCOPE:

DESIGN AND CONSTRUCT FOR FALL
2017 OCCUPANCY

KEITH HITLS
DISTRICT ADMINISTRATOR
715-682-7080
KHILTS@SDAK.12.NET

RECENT ACTIVITY:


- 14% shop drawings submitted
- 10% shop drawings reviewed
- Removed existing storm piping and installed 499' of 12" HDPE.
- Stripped footing forms and backfilled east addition.
- Installed wall forms, rebar and poured west foundation walls.
- Installed damproofing.

CRITICAL UPCOMING EVENTS:

- Strip forms and backfill foundation walls in west addition.
- Install underground electric to east addition.
- Install steel on east addition.

KEY DATES:

- Next meeting - 5-11-17
- Asbestos Abatement - 6-5-17

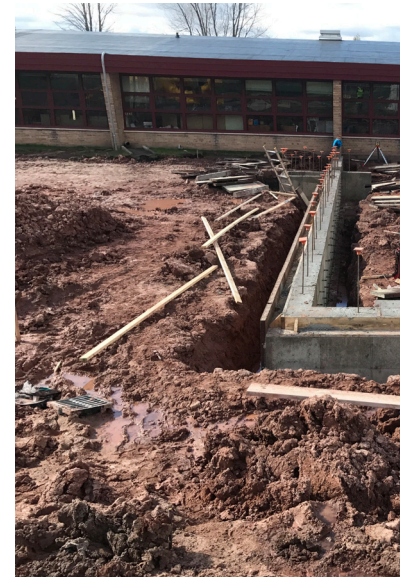

Construction: Phase I

Occupancy

Construction: Phase IA

Occupancy

Construction: Phase 2

Occupancy

4/2017

5/2017

6/2017

7/2017

8/2017

9/2017

10/2017

11/2017


We are here
