

Marengo Valley Elementary Remodeling & Addition

Activity Report

June 5, 2017

OBJECTIVE:

RENOVATION AND ADDITION TO
MARENGO VALLEY ELEMENTARY
SCHOOL

SCOPE:

DESIGN AND CONSTRUCT FOR FALL
2017 OCCUPANCY

KEITH HITLS
DISTRICT ADMINISTRATOR
715-682-7080
KHILTS@SDAK.12.NET

RECENT ACTIVITY:


- 55% shop drawings submitted
- 54% shop drawings reviewed
- Installed exterior sheathing and roof edge.
- Electrical rough-in masonry walls.
- installed south CMU wall in multipurpose room.

CRITICAL UPCOMING EVENTS:

- Install slab on grade
- Interior demolition.
- East addition roof.

KEY DATES:

- Next meeting - 6-8-17
- Asbestos Abatement - 6-5-17

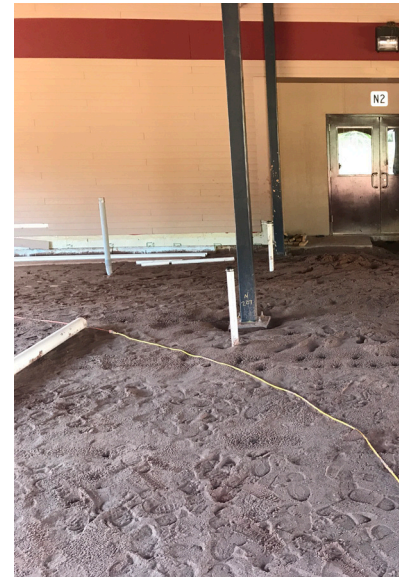

Construction: Phase I

Occupancy

Construction: Phase IA

Occupancy

Construction: Phase 2

Occupancy

4/2017

5/2017

6/2017

7/2017

8/2017

9/2017

10/2017

11/2017

↑
We are here
