

**OBJECTIVE:**

RENOVATION OF EXISTING HIGH SCHOOL WITH FIELDHOUSE & SECURE ENTRY ADDITION

**SCOPE:**

DESIGN AND CONSTRUCT FOR FINAL OCCUPANCY FALL 2018

KEITH HILTS  
DISTRICT ADMINISTRATOR  
715-682-7080  
KHILTS@SDAK.12.NET

**RECENT ACTIVITY:**


- Insulated and sheetrocked in classrooms, FACE room and art room
- Framed and set door frames for security doors
- Paved 2nd lift of asphalt
- Continued conduit and pulling wire
- Continued overhead lighting rough-in for corridors
- Worked on auditorium lights
- Installed heat tape in fieldhouse
- Installed duct and pipe in corridors
- Finished temperature control rough-in
- Started ceramic tile in middle corridor
- Drilled sleeves in field house for tennis standards

**CRITICAL UPCOMING EVENTS:**

- Grade exterior
- Continue work in auditorium
- Start painting classrooms behind taping
- Refinish commons floor

**KEY DATES:**

- Next meeting: 7-25-18

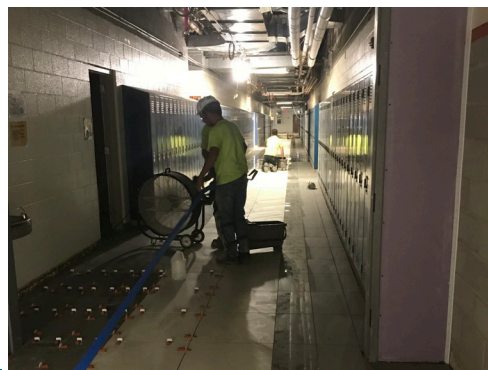

↑  
We are here
