

# Lake Superior Elementary Remodeling & Additions

Activity Report

July 17, 2017

## OBJECTIVE:

RENOVATION AND ADDITIONS  
TO LAKE SUPERIOR ELEMENTARY  
SCHOOL

## SCOPE:

DESIGN AND CONSTRUCT FOR FALL  
2017 OCCUPANCY

KEITH HILTS  
DISTRICT ADMINISTRATOR  
715-682-7080  
KHILTS@SDAK.12.NET

## RECENT ACTIVITY:


- 35% shop drawings submitted
- 34% shop drawings reviewed
- Install drain tile and backfill in Area H.
- Installed plumbing venting in Area G and sleeves in Area H.
- Continued ductwork and piping in Areas D and G.
- Insulated heating piping.
- Moved Electrical CT cabinet and starting pulling wire.
- Installed wood windows in Areas D and G.
- Started casework installation.

## CRITICAL UPCOMING EVENTS:

- Wood door delivery.
- Masonry installation in Area H.
- Cleaning

## KEY DATES:

- Next meeting 7-19-17

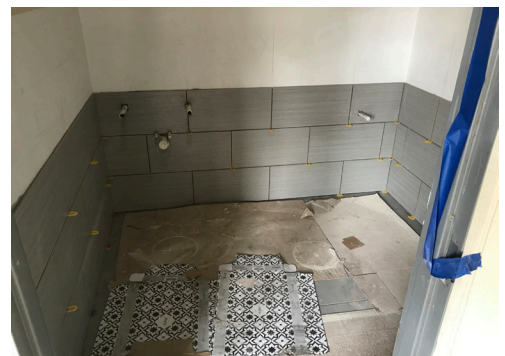

Construction: Phase I

Occupancy

Construction: Phase IA

Occupancy

Construction: Phase 2

Occupancy

4/2017

5/2017

6/2017

7/2017

8/2017

9/2017

10/2017

11/2017

↑  
We are here
