

*School District  
of Ashland*

## ASHLAND HIGH SCHOOL



*Adding Value to Everything We Do*

### The following is a list of work performed in the last 30 days:

- Pave front entry and north lot
- Landscape front entry and north end
- Set long span joists and deck field house
- Roof field house addition
- Frame and sheetrock IMC
- Install lockers
- Pour storage area and corridor in A2
- Underground MEP rough in, in fieldhouse
- Punch list items in phase 1
- Lay block for elevator shaft

### The following is a list of work scheduled for the next 30 days:

- Set glu lams
- Set steel for commons and office area
- Grade field house and office area
- Pour field house
- Set curtain wall at fieldhouse
- Set tinker space storefront in IMC
- Lay block for knee wall at curtain wall
- Roof field house
- Set split joists in A2
- Structural stud framing at fieldhouse

### Schedule:

Phase IA Complete.....	November 15, 2017
Phase II Complete.....	March 15, 2018
Phase III Complete.....	August 15, 2018




Prepping for Glu Lams



Roofing Fieldhouse




Looking North

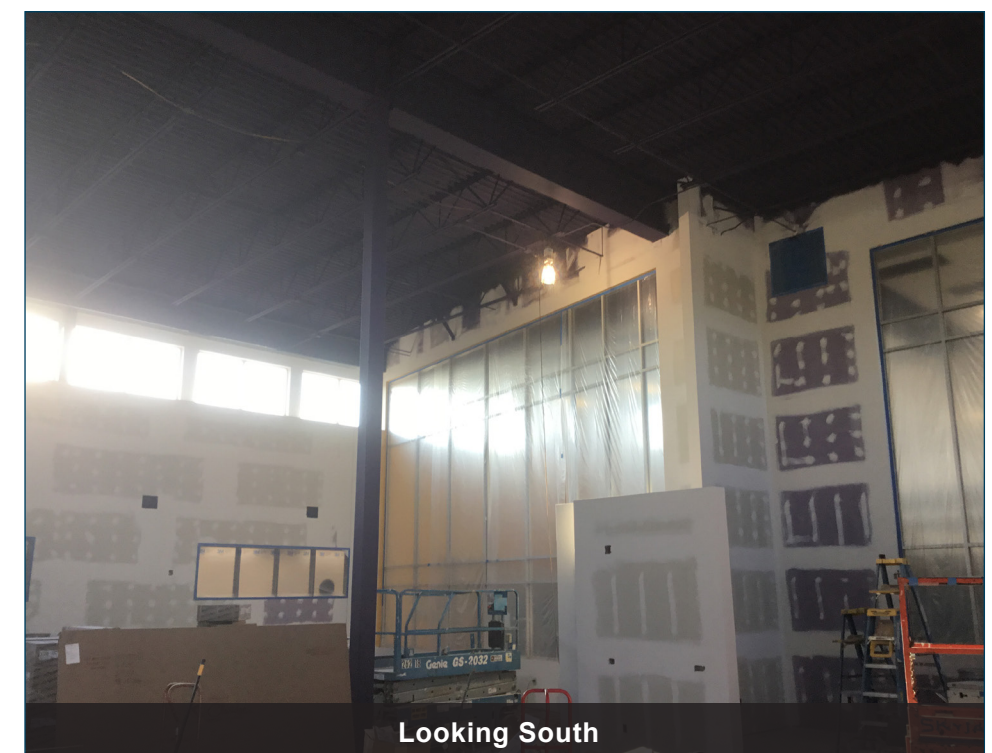

Looking South





*School District  
of Ashland*

## MARENGO VALLEY ELEMENTARY SCHOOL



*Adding Value to Everything We Do*

### The following is a list of work performed in the last 30 days:

- Install aluminum doors
- Install countertops and casework
- Reroof
- Install doors and hardware
- Paint interior
- Relocate trail
- Grade and top soil exterior
- Sod and landscape exterior
- MEP rough in
- Install playground equipment

### The following is a list of work scheduled for the next 30 days:

- Side multipurpose
- Paint multipurpose
- Remove asphalt
- MEP rough in
- Install scoreboard
- Install rock wall
- Install flooring
- Install ceiling grid
- MEP finishes
- Repave west side

### Schedule:

Phase 2 Complete..... November 15, 2017



Prepping for Siding



Painting Multipurpose




Corridor 136 Looking South



Installing Playground Equipment



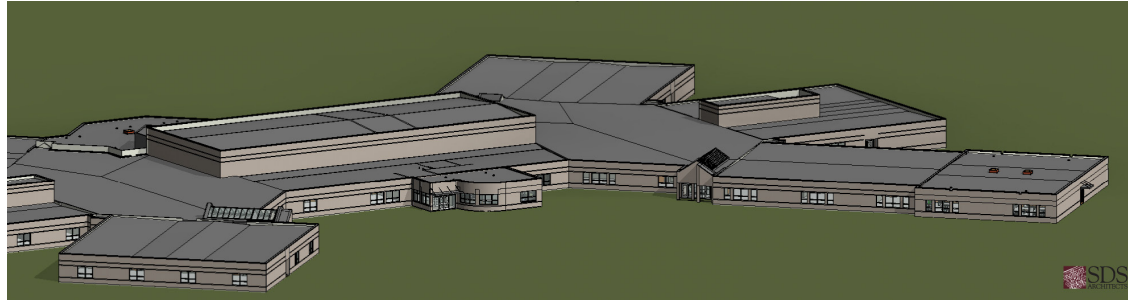

## LAKE SUPERIOR ELEMENTARY SCHOOL



### The following is a list of work performed in the last 30 days:

- Set pre cast in area H
- Lay block bearing walls
- Punch list items
- MEP rough in area H
- Install plumbing fixtures
- Pour sidewalks and pave
- Install flooring
- Install doors and hardware
- Spray foam block walls area H
- Pour slab on grade area H

### The following is a list of work scheduled for the next 30 days:

- MEP rough in area H
- Set steel in area H
- Pour topping at pre cast
- Lay brick area H
- Install windows
- Set AHU
- Install door frames area H
- Install roof edge and drains
- Roof area H
- Lay block partitions

### Schedule:


Phase II Complete ..... November 15, 2017




Area H Looking South



Finished Block Bearing Walls Area H

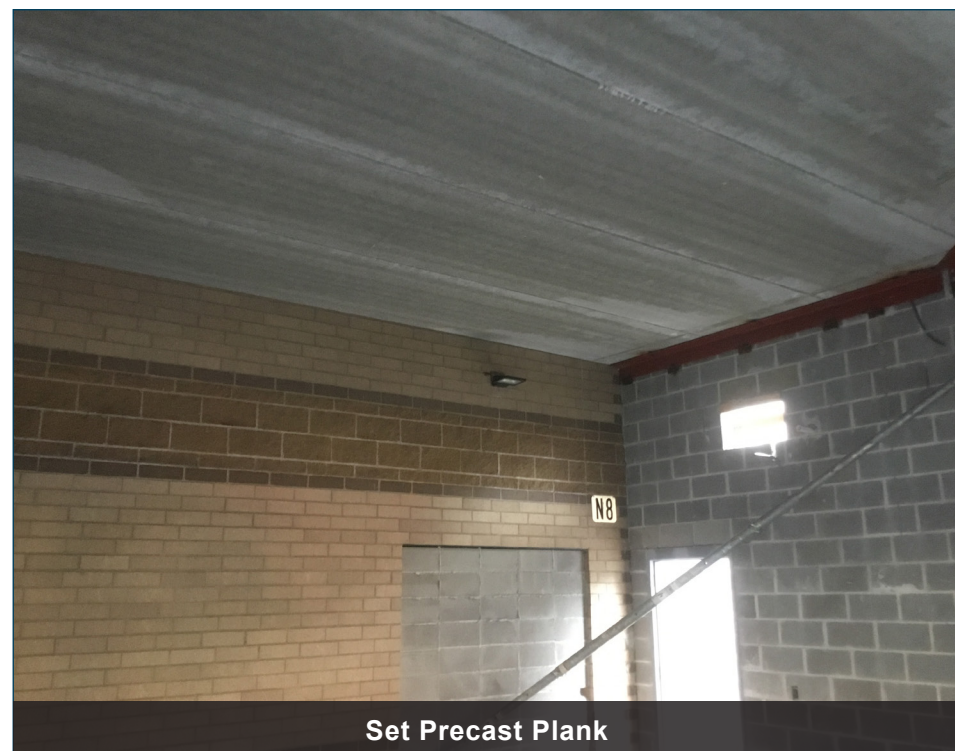

Set Precast Plank

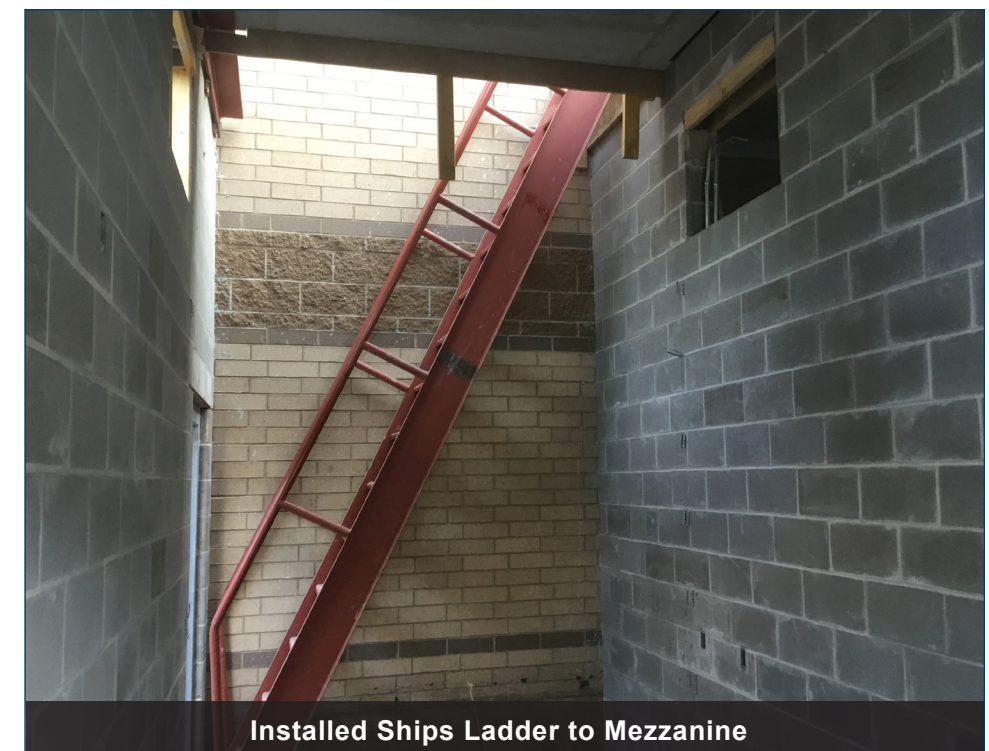

Installed Ships Ladder to Mezzanine
